

# Archbishop Hoban High School CREATE Studios Project



**Project # 20-033**

One Holy Cross Boulevard

Akron, Ohio 44306

**Weekly Update**

January 13, 2021

# Week of 01.13.2021

## Two-week Look-Behind / Look-Ahead


### 2 Week Look Behind

- Rough framing completed and inspection passed.
- Rough electrical complete and inspection passed
- Masonry work complete
- Ceiling patch work on 2<sup>nd</sup> floor under plumbing work is complete, which includes re-installation of ceiling tiles (drywall hung, but not finished so it can be removed, in areas under structural work which is still being determined)
- Drywall patch work in areas of old wall unit heaters and exterior vents

### 2 Week Look Ahead

- Install insulation
- Install drywall
- Drywall skim coating
- HVAC rough-in
- Structural steel reinforcing (TBD)



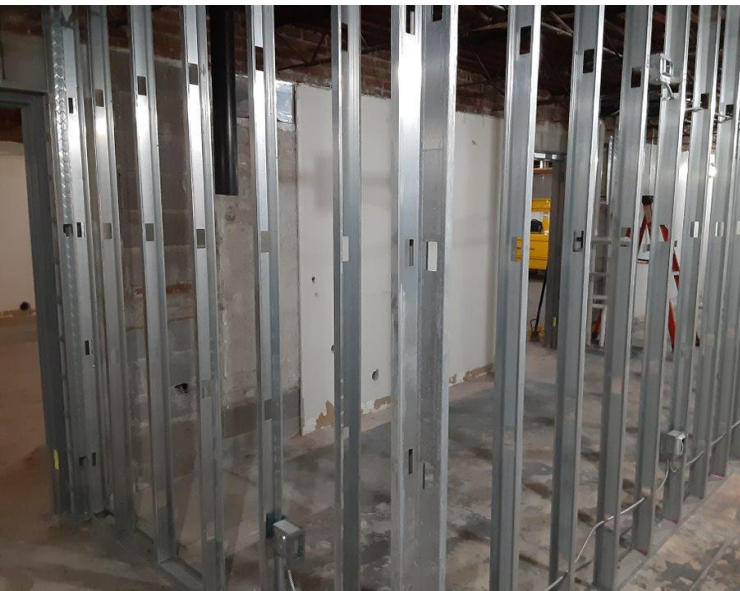

**Photos from 01.13.2021**





